DRAFT FOR DISCUSSION PURPOSES - INFORMATION AS OF 05/13/02

ID	Task Name	% Complete	Duration	Start	Finish	Predecessors
1	**Short Term Study: EHC (EHCJLI/01/02)**	**65%**	**241 days**	**Thu 11/1/01**	**Fri 9/27/02**	
2	Investigator Brochure	100%	15 days	Thu 11/1/01	Wed 11/21/01	
3	Study Objectives	100%	5 days	Thu 11/1/01	Wed 11/7/01	
4	Draft protocol / Summary Plan	100%	10 days	Thu 11/8/01	Wed 11/21/01	3
5	Site Selection	100%	15 days	Thu 11/22/01	Wed 12/12/01	4
6	Agreement with CRO (protocol development)	100%	32 days	Thu 12/13/01	Fri 1/25/02	5,4
7	Protocol Development	100%	52 days	Thu 11/22/01	Fri 2/1/02	2,4
8	Final Draft Protocol, Informed Consent	100%	0 days	Tue 2/12/02	Tue 2/12/02	7
9	IRB Review	100%	8 days	Mon 2/4/02	Wed 2/13/02	8,2
10	Bioanalytical Methods Set-up at MDS	50%	80 days	Thu 11/22/01	Wed 3/13/02	4
11	IRB Approval	100%	0 days	Wed 2/13/02	Wed 2/13/02	9
12	Final Protocol, Informed Consent	100%	0 days	Wed 2/13/02	Wed 2/13/02	11
13	Project Agreement (Study Execution)	100%	8 days	Tue 2/12/02	Thu 2/21/02	8
14	Lighter Training	100%	2 days	Mon 2/25/02	Tue 2/26/02	
15	Recruitment and Screening	100%	20 days	Thu 2/14/02	Wed 3/13/02	11
16	Test Materials Available	100%	0 days	Thu 2/14/02	Thu 2/14/02	
17	Data Analysis Plan	100%	25 days	Tue 2/12/02	Sat 3/16/02	8
18	**ETS Measurement**	**99%**	**154 days**	**Mon 12/3/01**	**Sun 6/30/02**	
19	Lease agreement (ORNL)	100%	65 days	Mon 12/3/01	Fri 3/1/02	
20	Delivery of equipment (ORNL)	0%	1 day	Mon 3/11/02	Mon 3/11/02	19
21	Lease agreement (California Analytical)	100%	36 days	Mon 12/3/01	Mon 1/21/02	
22	Delivery of equipment (California Analytical)	100%	1 day	Mon 3/11/02	Mon 3/11/02	21
23	ETS Sampling	100%	8 days	Sun 3/17/02	Sun 3/24/02	20,22,28SS
24	ETS Data analysis	100%	14 wks	Mon 3/25/02	Sun 6/30/02	23
25	**Clinical Testing**	**100%**	**11 days**	**Thu 3/14/02**	**Mon 3/25/02**	**15,11,16**
26	Subject Check In	100%	1 day	Thu 3/14/02	Thu 3/14/02	
27	Subject Randomization	100%	0 days	Sat 3/16/02	Sat 3/16/02	
28	Study Conduct	100%	8 days	Sun 3/17/02	Sun 3/24/02	14
29	Subject Release	100%	0 days	Mon 3/25/02	Mon 3/25/02	
30	**Lab Analysis**	**19%**	**40 days**	**Mon 3/25/02**	**Fri 5/17/02**	**10,25**
31	Analysis of Biomarkers	25%	6 wks	Mon 3/25/02	Fri 5/3/02	
32	Data Listings to PM	0%	1 wk	Mon 5/6/02	Fri 5/10/02	31
33	Biomarker Tables to PM	0%	1 wk	Mon 5/13/02	Fri 5/17/02	32
34	**Data Management**	**6%**	**65 days**	**Mon 3/25/02**	**Fri 6/21/02**	**25,30SS**
35	Data Entry	20%	4 wks	Mon 3/25/02	Fri 4/19/02	
36	Edit Chks, Db Clean-Up	0%	4 wks	Mon 4/22/02	Fri 5/17/02	35
37	Internal Data Listing Review	0%	1 wk	Mon 5/20/02	Fri 5/24/02	36
38	DB Lock	0%	0 days	Fri 5/24/02	Fri 5/24/02	37
39	Data Listings for PM Review	0%	2 wks	Mon 5/27/02	Fri 6/7/02	38
40	Safety Table for PM Review	0%	2 wks	Mon 6/10/02	Fri 6/21/02	39
41	Data Analysis	0%	30 days	Mon 5/27/02	Fri 7/5/02	38
42	Draft Report	0%	30 days	Mon 6/24/02	Fri 8/2/02	34,24FF
43	PM Review of Draft Report	0%	20 days	Mon 8/5/02	Fri 8/30/02	42
44	Results Available	0%	0 days	Fri 8/30/02	Fri 8/30/02	43
45	Final Report	0%	20 days	Mon 9/2/02	Fri 9/27/02	44
46	Final Results	0%	0 days	Fri 9/27/02	Fri 9/27/02	45

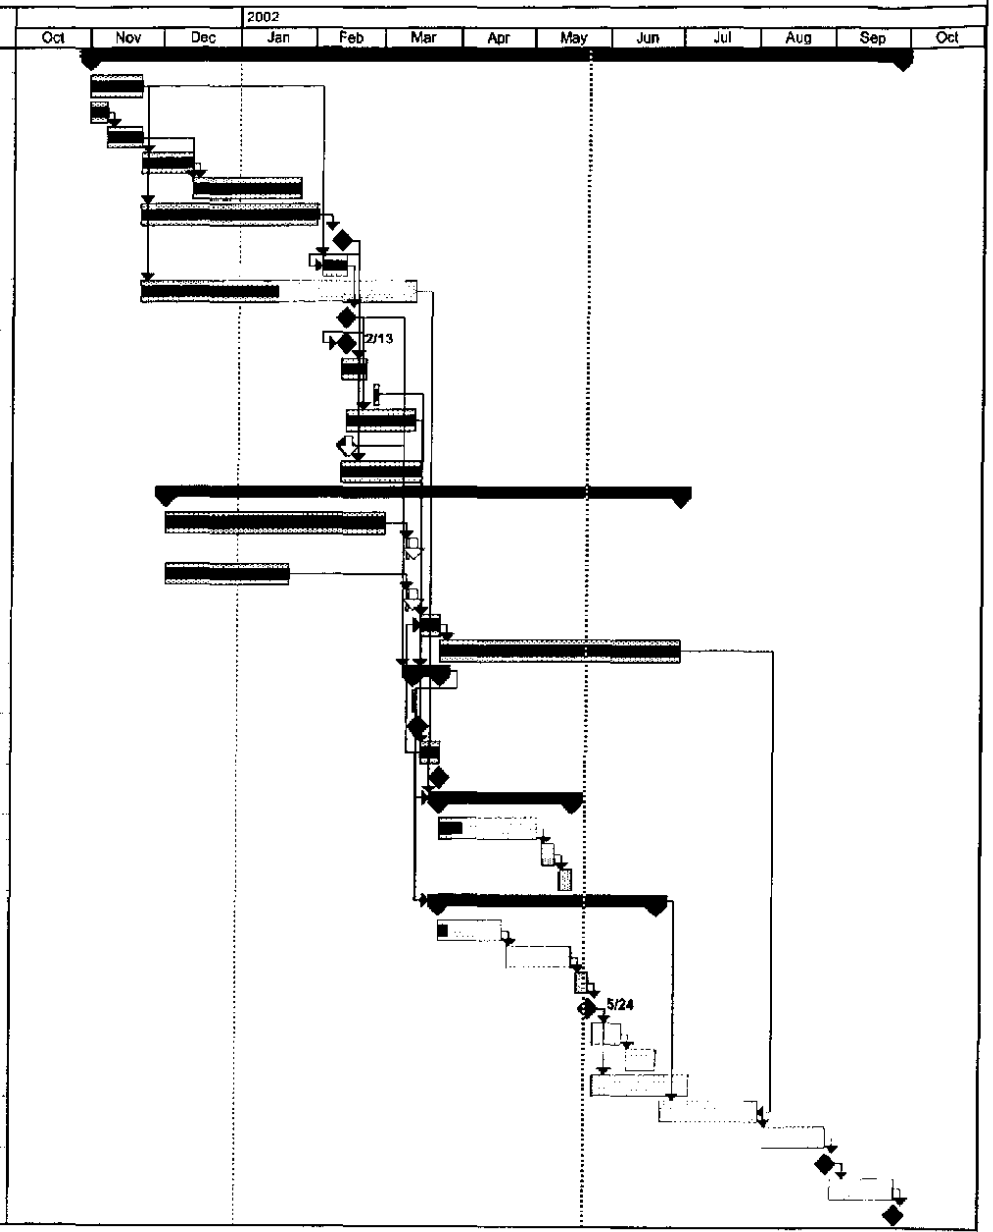

* Revisions

Project: Short Term2
Date: Thu 5/23/02

Task | Split | Progress | Milestone | Summary | Rolled Up Task | Rolled Up Split | Rolled Up Milestone | Rolled Up Progress | External Tasks | Project Summary | External Milestone | Deadline

Page 1

PM30067874 48

Source: https://www.industrydocuments.ucsf.edu/docs/gymx0001

ID	Task Name	Duration	Start	Finish
1	**Study Conduct**	**9 days?**	**Thu 3/14/02**	**Sun 3/24/02**
2	Subject Check-in	1 day?	Thu 3/14/02	Thu 3/14/02
3	Subject Randomization	1 day?	Sun 3/17/02	Sun 3/17/02
4	Study Conduct	6 days?	Mon 3/18/02	Sun 3/24/02
5	Subject Release	1 day?	Sun 3/24/02	Sun 3/24/02
6	Data Entry	4 wks	Mon 3/25/02	Fri 4/19/02
7	Edit Cks, DB Clean-up	4 wks	Mon 4/22/02	Fri 5/17/02
8	Internal Data Listing Review	1 wk	Mon 5/20/02	Fri 5/24/02
9	DB Lock	0 days	Fri 5/24/02	Fri 5/24/02
10	Data listings to PM for review	2 wks	Mon 5/27/02	Fri 6/7/02
11	Safety Table to PM for review	2 wks	Mon 6/10/02	Fri 6/21/02
12	Write Report	6 wks	Mon 6/24/02	Fri 8/2/02
13	Analysis of Biomarkers	6 wks	Mon 3/25/02	Fri 5/3/02
14	Data listings to PM	1 wk	Mon 5/6/02	Fri 5/10/02
15	Biomarker tables to PM	1 wk	Mon 5/13/02	Fri 5/17/02

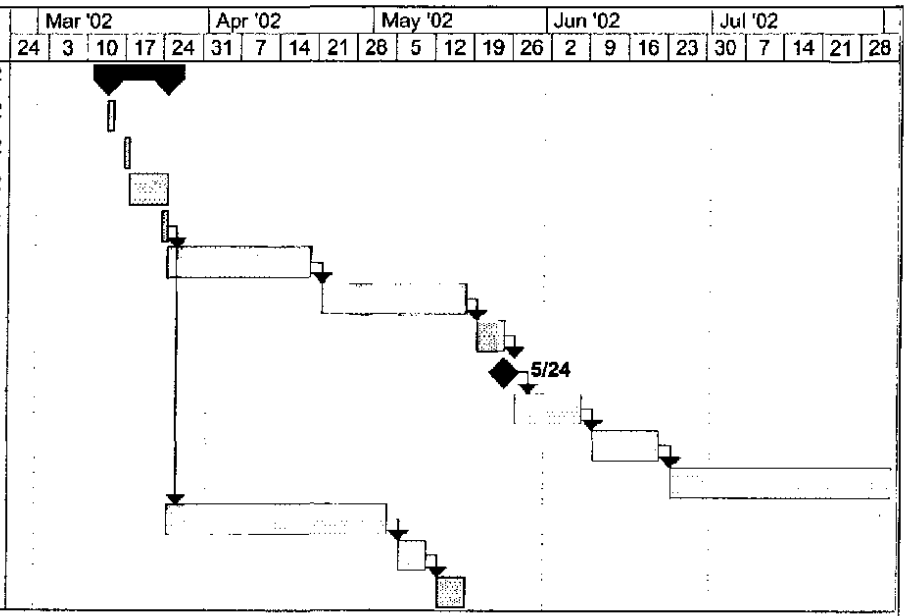

- Data Management -
- Draft Report

Project: MDS PS 28030
Date: Tue 1/8/02

Task
Split
Progress
Milestone
Summary
Project Summary
External Tasks
External Milestone
Deadline

Page 1

PM3006787449

Source: https://www.industrydocuments.ucsf.edu/docs/gymx0001
